



FLORIDA HIECC MEETING FEBRUARY 20, 2015

HARRIS TEAM UPDATE







HIGHLIGHTS




- Event Notification Service (ENS)
 - Completed all test connectivity sessions to connect hospital data sources for admit, discharge, and transfer (ADT) feeds
 - 63% of hospital connections are in Production
 - Received signed subscription agreements from WellCare and Sunshine State Health Plans
- Patient Look-Up (PLU)
 - Orlando Health went live in production on December 8, 2014
 - Tampa Bay RHIO completed milestones 6-11 of their Centers for Medicare and Medicaid Services (CMS) funded facilitated onboarding
- Direct Messaging Service (DMS)
 - Metrics included in following slides




DIRECT MESSAGING REGISTRANTS



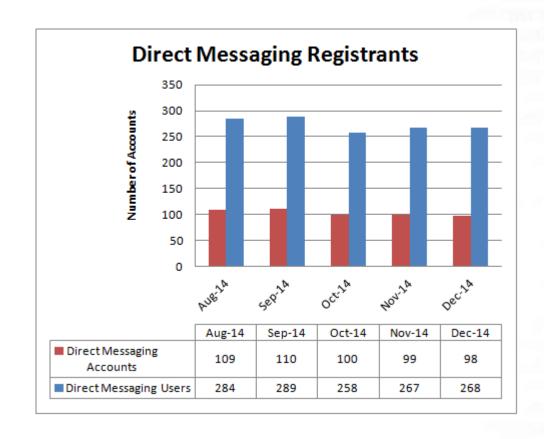

DIRECT MESSAGING TRANSACTIONS







ENS PRODUCTION DATA SOURCES



128 hospitals are in production

Data Sources	# of Hospitals
Adventist Health System	15
All Children's Health System	1
Ann Bates Leach Eye Hospital	1
Bay Care Health System	10
Bayfront Health St. Petersburg	1
Bert Fish Medical Center	1
Bethesda Health	2
Broward Health	4
Central Florida Health Alliance	3
Citrus Memorial Hospital	1
Desoto Memorial Hospital	1
Doctors Memorial Bonifay	1
Doctors Memorial Hospital (Perry)	1
Flagler Hospital	1
Halifax Hospital Medical Center	1
HCA	44
Health Central Hospital	1
Health First	4
Healthmark Regional Medical Center	1
Hendry Regional Medical Center	1

Data Sources	# of Hospitals
Indian River Memorial Hospital	1
Lake Butler Hospital	1
Lake Wales Medical Center	1
Lakeland Regional Medical Center	1
Lakeside Medical Center	1
Lee Memorial Health System	4
Manatee Healthcare System/Lakewood	2
Martin Health	3
Memorial Healthcare System	5
Miami Children's Hospital	1
Munroe Regional Medical Center	1
Parrish Medical Center	1
Putnam Community Medical Center	1
St. Vincents Health System	3
Tallahassee Memorial Healthcare	1
Tampa General Hospital	1
UF Health	2
University of Miami	1
University of Miami Hospital & Clinics	1
Wellington Regional Medical Center	1

ENS DATA SOURCE CONNECTIONS



100% of data sources completed test connections by January 31, 2015



PLU PRODUCTION DEPLOYMENTS



- Strategic Health Intelligence (SHI)
- Atlantic Coast HIE (ACH)
- Florida Hospital/Adventist
- UF Health
- Broward Health
- Martin Health
- Bethesda Health
- Senior Home Care an affiliate of Kindred at Home
- Orlando Health Live in production on December 8, 2014



PLU DEPLOYMENTS NEAR COMPLETION



 Community Health Systems (CMS) formerly known as Health Management Associates (HMA) – pending "go live"

Community Health Systems (formerly HMA) Deployment Status (Express Lite)

Kickoff Delivered/ Gateway Webinars	Service PD Registry GUI Dev Adapter Dev	Adapter Adapter Validation	Go Live
-------------------------------------	---	----------------------------	---------



PLU DEPLOYMENTS IN WORK



- Department of Health (DOH) Continued coordination of open tickets with Mirth on behalf of site; supported installing latest Mirth Connect, Mirth Match and Mirth Results in production environment; delivered to DOH an enhancement to the age range filter; attended DOH's on-site user training
- Florida Accountable Care Services (ACO) no requests for support this quarter
- Tampa Bay Regional Health Information Organization (RHIO) –
 Presented several webinars; started working through smoke tests between
 Tampa General Hospital and the Harris reference test system; completed
 onboarding milestones through document retrieve messaging
 implementation; prepped for pre-validation
- Community Health IT (Relay Health) Provided information on how to install Aurion manually; provided tentative project schedule listing webinars/major tasks; presented several webinars

PLU DEPLOYMENTS IN WORK




DOH Deployment Status (Express) Service Kickoff Webinars GUI Dev Validation Go Live Gateway Registry Adapter Adapter Adapter Dev Dev Florida Accountable Care Services Deployment Status (Express Lite) Self/Cross Service **GUI Dev** Kickoff Webinars Registry Validation Go Live Delivered/ Adapter Adapter Adapter Info Dev Dev Dev Tampa Bay RHIO Deployment Status (Site Services) OVA Delivered/ DQ Service Kickoff Registry **GUI Dev** Go Live Webinars Validation Adapter Adapter Adapter Installed Info Dev Community Health IT (Site Services) Self/Cross Service Kickoff Registry Delivered/ Webinars **GUI Dev** Adapter Adapter Adapter Validation Go Live Gateway Installed Test Info Dev Dev Dev



PLU TRANSACTIONS



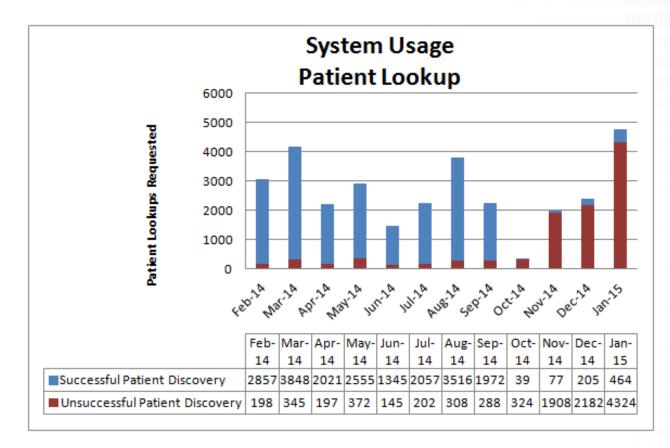

Note: Successful PDs are lower than prior periods due to a lower number of requests from SHI. All of the anesthesiologist SHI queries originate with patient data that is known to be in Broward Health.



PLU TRANSACTIONS




January 2015 Node Inbound Transactions

Node	Successful	Unsuccessful	Total Inbound Patient Discovery
SHI	15	593	608
ACH	27	582	609
Florida Hospital	2	26	28
UF Health	0	605	605
Broward Health	11	586	597
Martin Health System	3	591	594
Bethesda Health	0	596	596
Senior Home Care	12	563	575
Orlando Health	394	182	576
Totals	464	4324	4788

PLU TRANSACTIONS



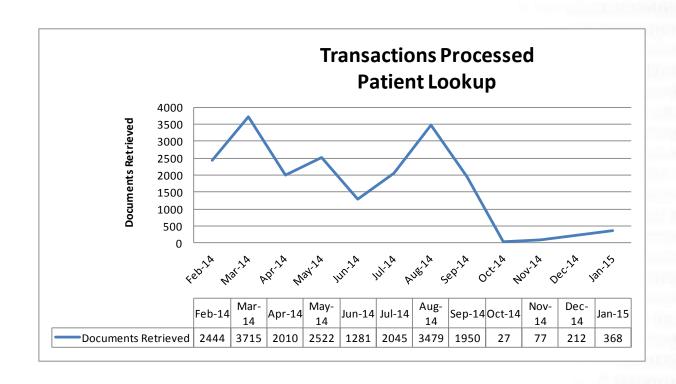









UPCOMING TECHNICAL ACTIVITIES – PLU



PLU deployment schedule:

				(Q1'1	.3	C	(2'13	3		(3'1	3	Q	4'1	3	Q	1'14	ļ.	Q	2'14	1	Q	3'1	4	С	4'14	1	Q	1'15	5	Q	2'15	5
#	Facilitated On-Boarding Node Name	Go Live		J	F	М	Α	М	J	J	Α	S	0	N	D	J	F	М	Α	М	J	J	Α	S	0	N	D	J	F	M	А	М	J
1	Strategic Health Intelligence (SHI)	May-12	Express Lite																														
2	Atlantic Coast HIE (ACH)	Mar-13	Express Lite	-	-	Χ																										П	
3	Florida Hospital	May-13	Express Lite	ı	ı	-	1	Χ																									
4	UF Health	May-13	Express Lite	ı	ı	-	1	Χ																									
5	Broward Health	Sep-13	Site Services			Χ	1	-	1	-	-	Х																					
6	Martin Health	Mar-14	Express Lite			Χ	1	1	-	-	-	-	-	-	-	-	-	Х															
7	Bethesda Health	May-14	Express Lite										Х	-	-	-	-	-	-	Х													
8	Senior Home Care	Jul-14	Express Lite				Χ	1	-	-	-	-	-	-	-	-	-	-	-	-	-	Х											
9	Orlando Health	Dec-14	Express Lite												Х	-	-	-	-	-	-	-	-	-	-	-	Х						
10	Community Health Systems (CHS)		Express Lite			Χ	1	1	-	1	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	Х				
11	Department of Health (DOH)		Express	ı	ı	1	1	-	ı	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	Х	
12	Tampa Bay RHIO		Site Services																Х	-	-	-	-	-	-	-	-	-	-	-	Х		
13	Community Health IT		Site Services																	Х	-	-	-	-	-	-	-	-	-	Х			
14	FL Accountable Care Services (FACS)		Express Lite								Χ	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	Х	
	# Concurrent			4	4	7	7	7	5	5	6	6	6	6	7	7	7	7	7	8	7	7	6	6	6	6	6	5	5	4	2	1	0

Note: Dates above represents best estimates for planning and logistical purposes and will be updated on an ongoing basis as new data is learned



UPCOMING TECHNICAL ACTIVITIES – ENS



- Data Sources
 - Assist remaining hospitals (75) to get into Production by March 31, 2015

ENS Data Source Deployment Plan as of January 31, 2015											
# of Hospitals	# of Hospitals Production Connected										
203	128	203									

Health Plans

ENS Health Plan Deployment Plan									
Organization	Initial Member #	Target Start Date							
Well Care	50,000	February 2015							
Sunshine State Health Plan	400,000	March 2015							





