



FLORIDA HIECC MEETING NOVEMBER 21, 2014

HARRIS TEAM UPDATE







HIGHLIGHTS




- Direct Secure Messaging (DSM)
 - Completed the transition of DSM to the new Direct Messaging vendor Inpriva
 - Processed an archive retrieval request from the Agency for Persons with Disabilities (APD)
- Event Notification Service (ENS)
 - Piloted virtual private network (VPN) connection and requirements
 - Scheduled ENS Connectivity sessions with hospital sources through the end of January
 - Held connectivity sessions to connect hospital data sources for admit, discharge, and transfer (ADT) feeds
- Patient Look-Up (PLU)
 - Orlando Health completed pre-validation testing and started validation testing which includes testing with Florida Hospital
 - Tampa Bay RHIO completed milestones 1-5 of their Centers for Medicare and Medicaid Services (CMS) funded facilitated onboarding



DIRECT MESSAGING REGISTRANTS




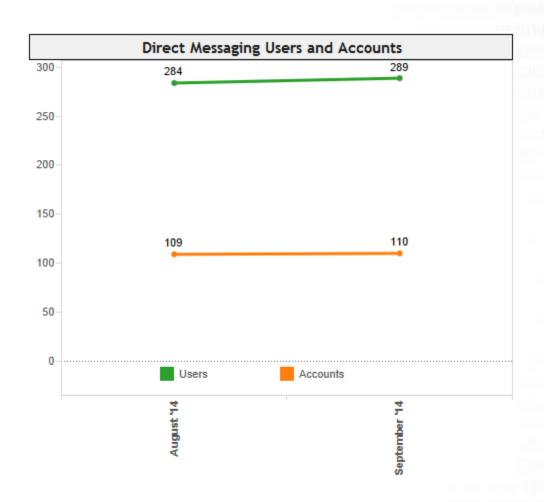



DIRECT MESSAGING TRANSACTIONS




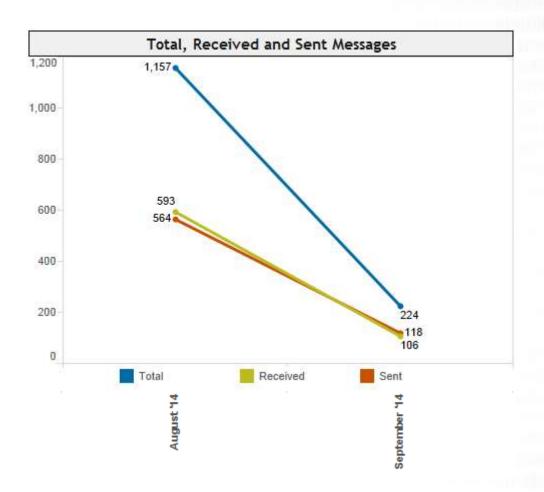



ENS TRANSACTIONS



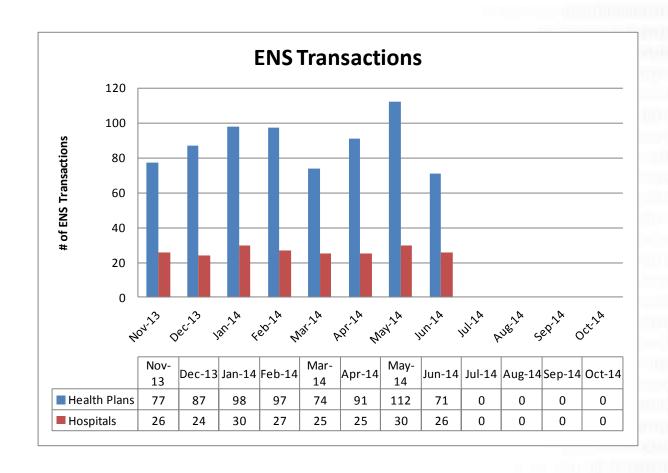



ENS PRODUCTION DATA SOURCES



Data Sources	# of Hospitals	Status
Adventist Health System	15	Production
Bethesda Health	2	Production
Broward Health	4	Production
Citrus Memorial Hospital	1	Production
Halifax Hospital Medical Center	1	Production
Health Central Hospital	1	Production
Lakeland Regional Medical Center	1	Production
Martin Health	3	Production
Parrish Medical Center	1	Production
Tampa General Hospital	1	Production
UF Health	2	Production

ENS DATA SOURCE CONNECTIONS



Data Sources	# of Hospitals	Status
All Children's Health System	1	Connected
Ann Bates Leach Eye Hospital	1	Connected
Baker County Ed Fraser	1	Connected
Bay Care Health System	10	Connected
Flagler Hospital	1	Connected
Florida Hospital	7	Connected
НСА	44	Connected
Healthcare District of Palm Beach County	1	Connected
Manatee Healthcare System	2	Connected
Mt. Sinai Medical Center	1	Connected
Naples Community Hospital	2	Connected
Orlando Health System	6	Connected
Sarasota Memorial Hospital	1	Connected
St. Vincents Health System	3	Connected
University of Miami	1	Connected
University of Miami Hospital & Clinics	1	Connected
Wellington Regional Medical Center	1	Connected



PLU PRODUCTION DEPLOYMENTS



- Strategic Health Intelligence (SHI)
- Atlantic Coast HIE (ACH)
- Florida Hospital/Adventist
- UF Health
- Broward Health
- Martin Health
- Bethesda Health
- Senior Home Care an affiliate of Kindred at Home



PLU DEPLOYMENTS NEAR COMPLETION



Community Health Systems (CMS) formerly known as Health
 Management Associates (HMA) – completed validation, pending "go live"

Community Health Systems (formerly HMA) Deployment Status (Express Lite)

OVA Self/Cross Compared And Self/Cross Compa	Service PD Registry GUI Dev Adapter Dev	DQ DR Adapter Adapter Dev Dev	Go Live
--	---	-------------------------------	---------



PLU DEPLOYMENTS IN WORK




- Department of Health (DOH) Continued coordination of open tickets with Mirth on behalf of site; waiting on next Mirth Match release that contains work item age range filter (expected this month)
- Orlando Health Completed pre-validation testing and started validation testing; testing with Florida Hospital
- Florida Accountable Care Services (ACO) no requests for support this quarter
- Tampa Bay Regional Health Information Organization (RHIO) –
 Completed self test, cross-gateway tests, audit log transfer manager and production audit transfer manager testing; covered roadmap webinar
- Community Health IT (Relay Health) Presented kick-off webinar to Relay team; started coordination to send Express Lite OVA file




PLU DEPLOYMENTS IN WORK



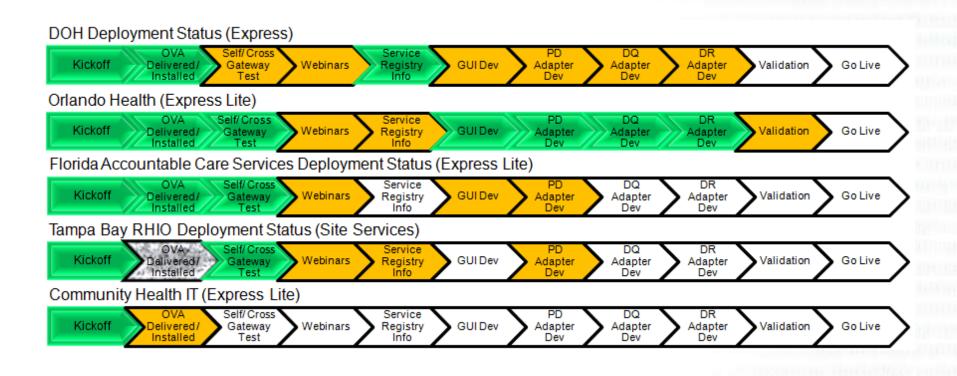

PLU TRANSACTIONS



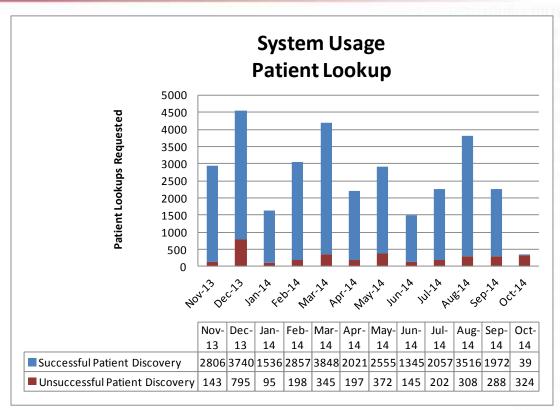

Note: The number of Patient Discovery queries decreased in October because queries from SHI to Broward decreased


October 2014 Node Inbound Transactions

Node	Successful	Unsuccessful	Total Inbound Patient Discovery										
SHI	14	39	53										
ACH	0	52	52										
Florida Hospital	0	25	25										
UF Health	12	42	54										
Broward Health	3	22	25										
Martin Health System	0	51	51										
Bethesda Health	0	52	52										
Senior Home Care	10	41	51										



PLU TRANSACTIONS



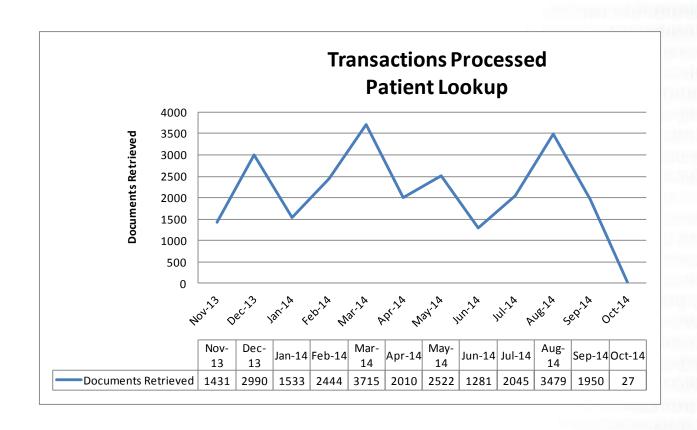









UPCOMING TECHNICAL ACTIVITIES – PLU



PLU deployment schedule:

				Q1'13									Q2'15																				
#	Facilitated On-Boarding Node Name	Go Live		J	Ť			М		J	A		o	_			_	_		M	_			_		N	_					M.	$\overline{}$
1	Strategic Health Intelligence (SHI)	May-12	Express Lite																														
2	Atlantic Coast HIE (ACH)	Mar-13	Express Lite	1	1	Χ																	İ										
	- SFREC/HCN			-	-	-	-	-	-	-	-	-	Х																				
3	Florida Hospital	May-13	Express Lite	-	-	-	-	Χ																									
4	UF Health	May-13	Express Lite	-	1	-	-	Χ																									
5	Broward Health	Sep-13	Site Services			Χ	-	-	-	-	-	Х																					
6	Martin Health	Mar-14	Express Lite			Χ	ı	-	-	-	-	-	-	-	-	-	-	Х															
7	Bethesda Health	May-14	Express Lite										Х	-	-	-	-	-	-	Х													
8	Senior Home Care	Jul-14	Express Lite				Χ	-	-	-	-	-	-	-	1	-	-	-	-	-	-	Х											
9	Community Health Systems (CHS)		Express Lite			Χ	ı	-	-	-	-	-	-	-	1	-	-	-	-	-	-	-	-	-	-	Х							
10	Orlando Health		Express Lite												Х	-	-	-	-	-	-	-	-	-	-	-	Х						
11	Department of Health (DOH)		Express	1	1	1	ı	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	1	-	Х	
12	Tampa Bay RHIO		Site Services																Х	-	-	-	-	-	-	-	-	Х					
13	Community Health IT		Express Lite																	Х	-	-	-	-	-	-	-	-	Х				
14	FL Accountable Care Services (FACS)		Express Lite								Χ	-	-	-	-	-	-	-	-	-	-	- [-	-	-	-	-	-	-	Х			
	# Concurrent			5	5	8	8	8	6	6	7	7	7	6	7	7	7	7	7	8	7	7	6	6	6	6	5	4	3	2	1	1 (0

Note: Dates above represents best estimates for planning and logistical purposes and will be updated on an ongoing basis as new data is learned



UPCOMING TECHNICAL ACTIVITIES – ENS



ENS Deployment Plan as of October 31, 2014

# of Hospitals	Production	Connected	November	<u>December</u>	January
204	32	84	43	22	23







